


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	'19	Apr 7, '19							
							M	T	W	T	F	S	S	M	T
1		Roofing	18 days	Tue 4/2/19	Thu 4/25/19										
2		Roofing : Bldg A (820/822)	3 days	Tue 4/2/19	Thu 4/4/19										
3		Roofing : Bldg B (816/818)	3 days	Tue 4/2/19	Thu 4/4/19										
4		Roofing : Bldg C (812/814)	3 days	Fri 4/5/19	Tue 4/9/19	3									
5		Roofing : Bldg D (808/810)	3 days	Fri 4/5/19	Tue 4/9/19	3									
6		Roofing : Bldg E (804/806)	3 days	Wed 4/10/19	Fri 4/12/19	4,5									
7		Roofing : Bldg F (800/802)	3 days	Wed 4/10/19	Fri 4/12/19	4,5									
8		Roofing : Bldg G (801/803)	3 days	Mon 4/15/19	Wed 4/17/19	6,7									
9		Roofing : Bldg H (805/807)	3 days	Mon 4/15/19	Wed 4/17/19	6,7									
10		Roofing : Bldg I (809/811)	3 days	Thu 4/18/19	Mon 4/22/19	8,9									
11		Roofing : Bldg J (813/815)	3 days	Thu 4/18/19	Mon 4/22/19	8,9									
12		Roofing : Bldg K (817/819)	3 days	Tue 4/23/19	Thu 4/25/19	10,11									
13		Siding/Windows	5 days	Mon 4/29/19	Fri 5/3/19										
14		Windows	2 days	Mon 4/29/19	Tue 4/30/19										
15		Siding/Windows	5 days	Mon 4/29/19	Fri 5/3/19										

Project: Hunningdon II Schedul
Date: Tue 4/2/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

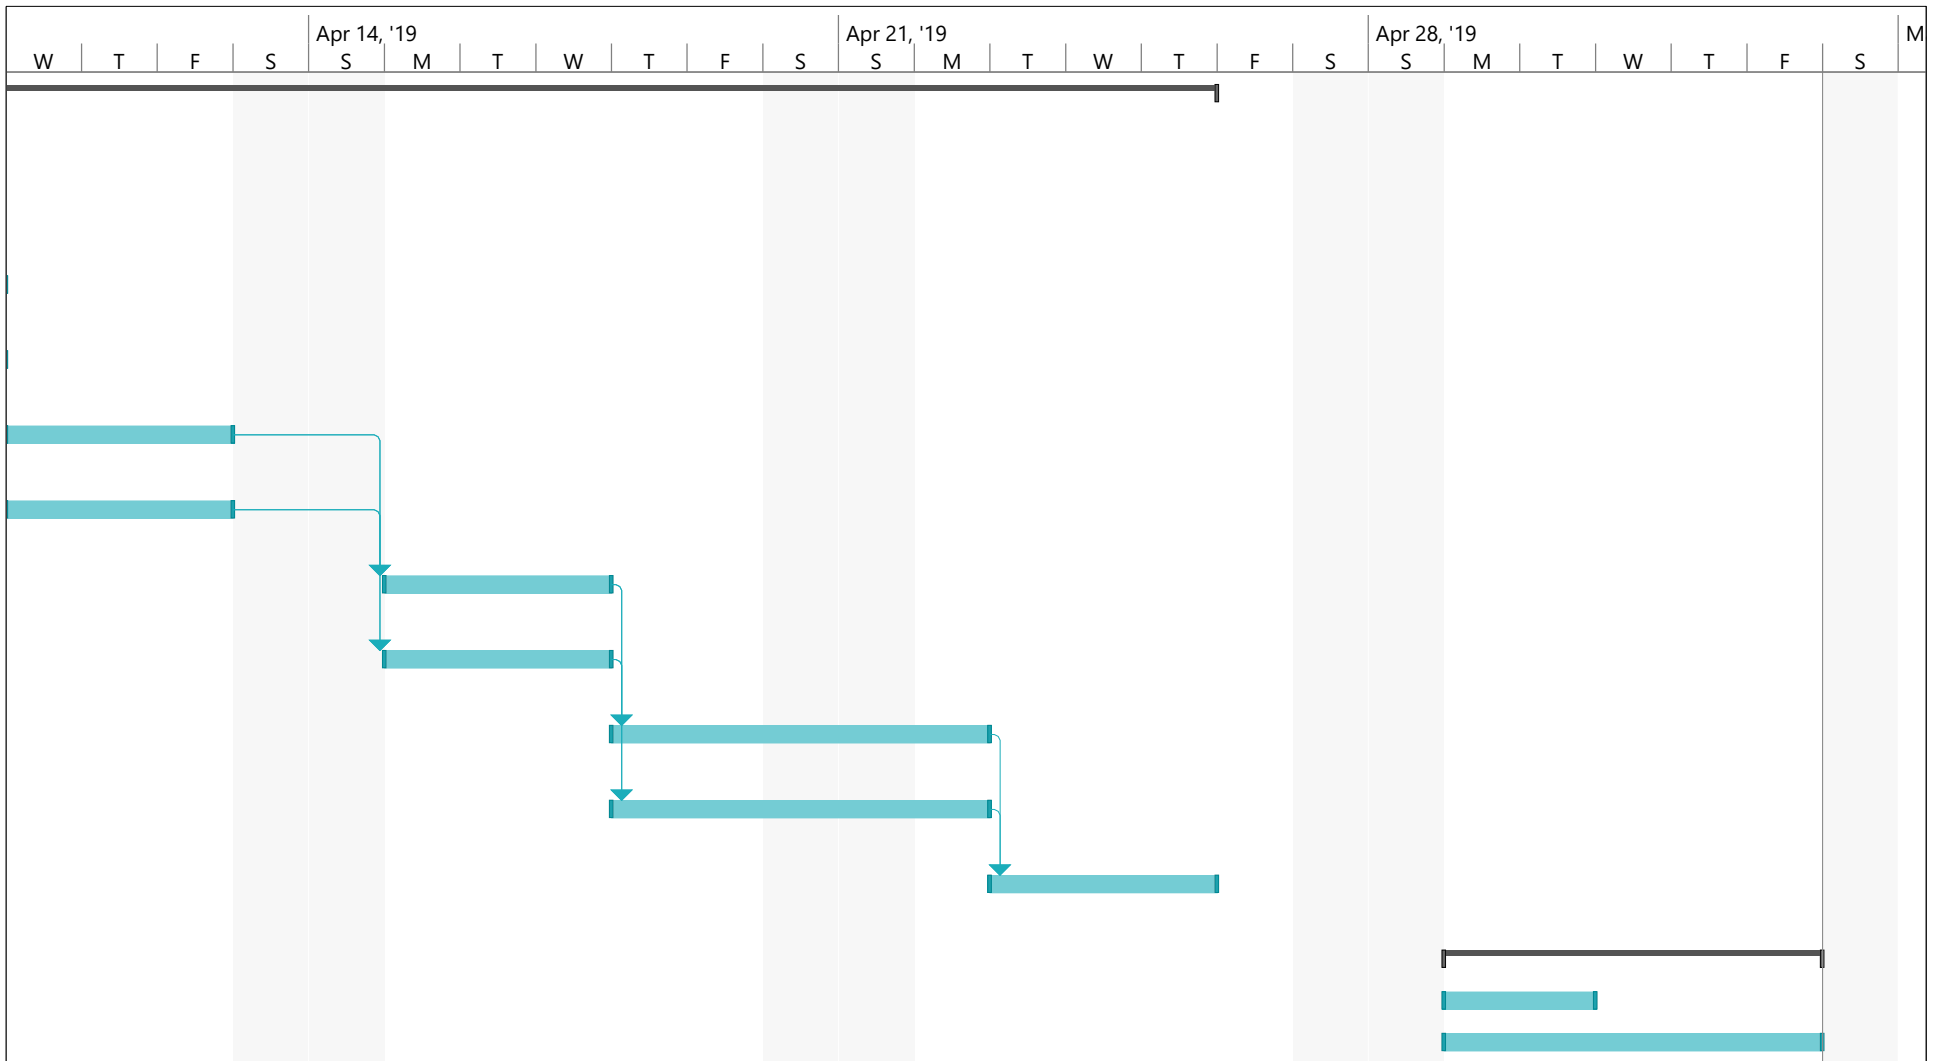

Project: Hunningdon II Scheduling Date: Tue 4/2/19	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
